


LEE COUNTY DIVISION OF SOLID WASTE MASTER PROJECT SCHEDULE

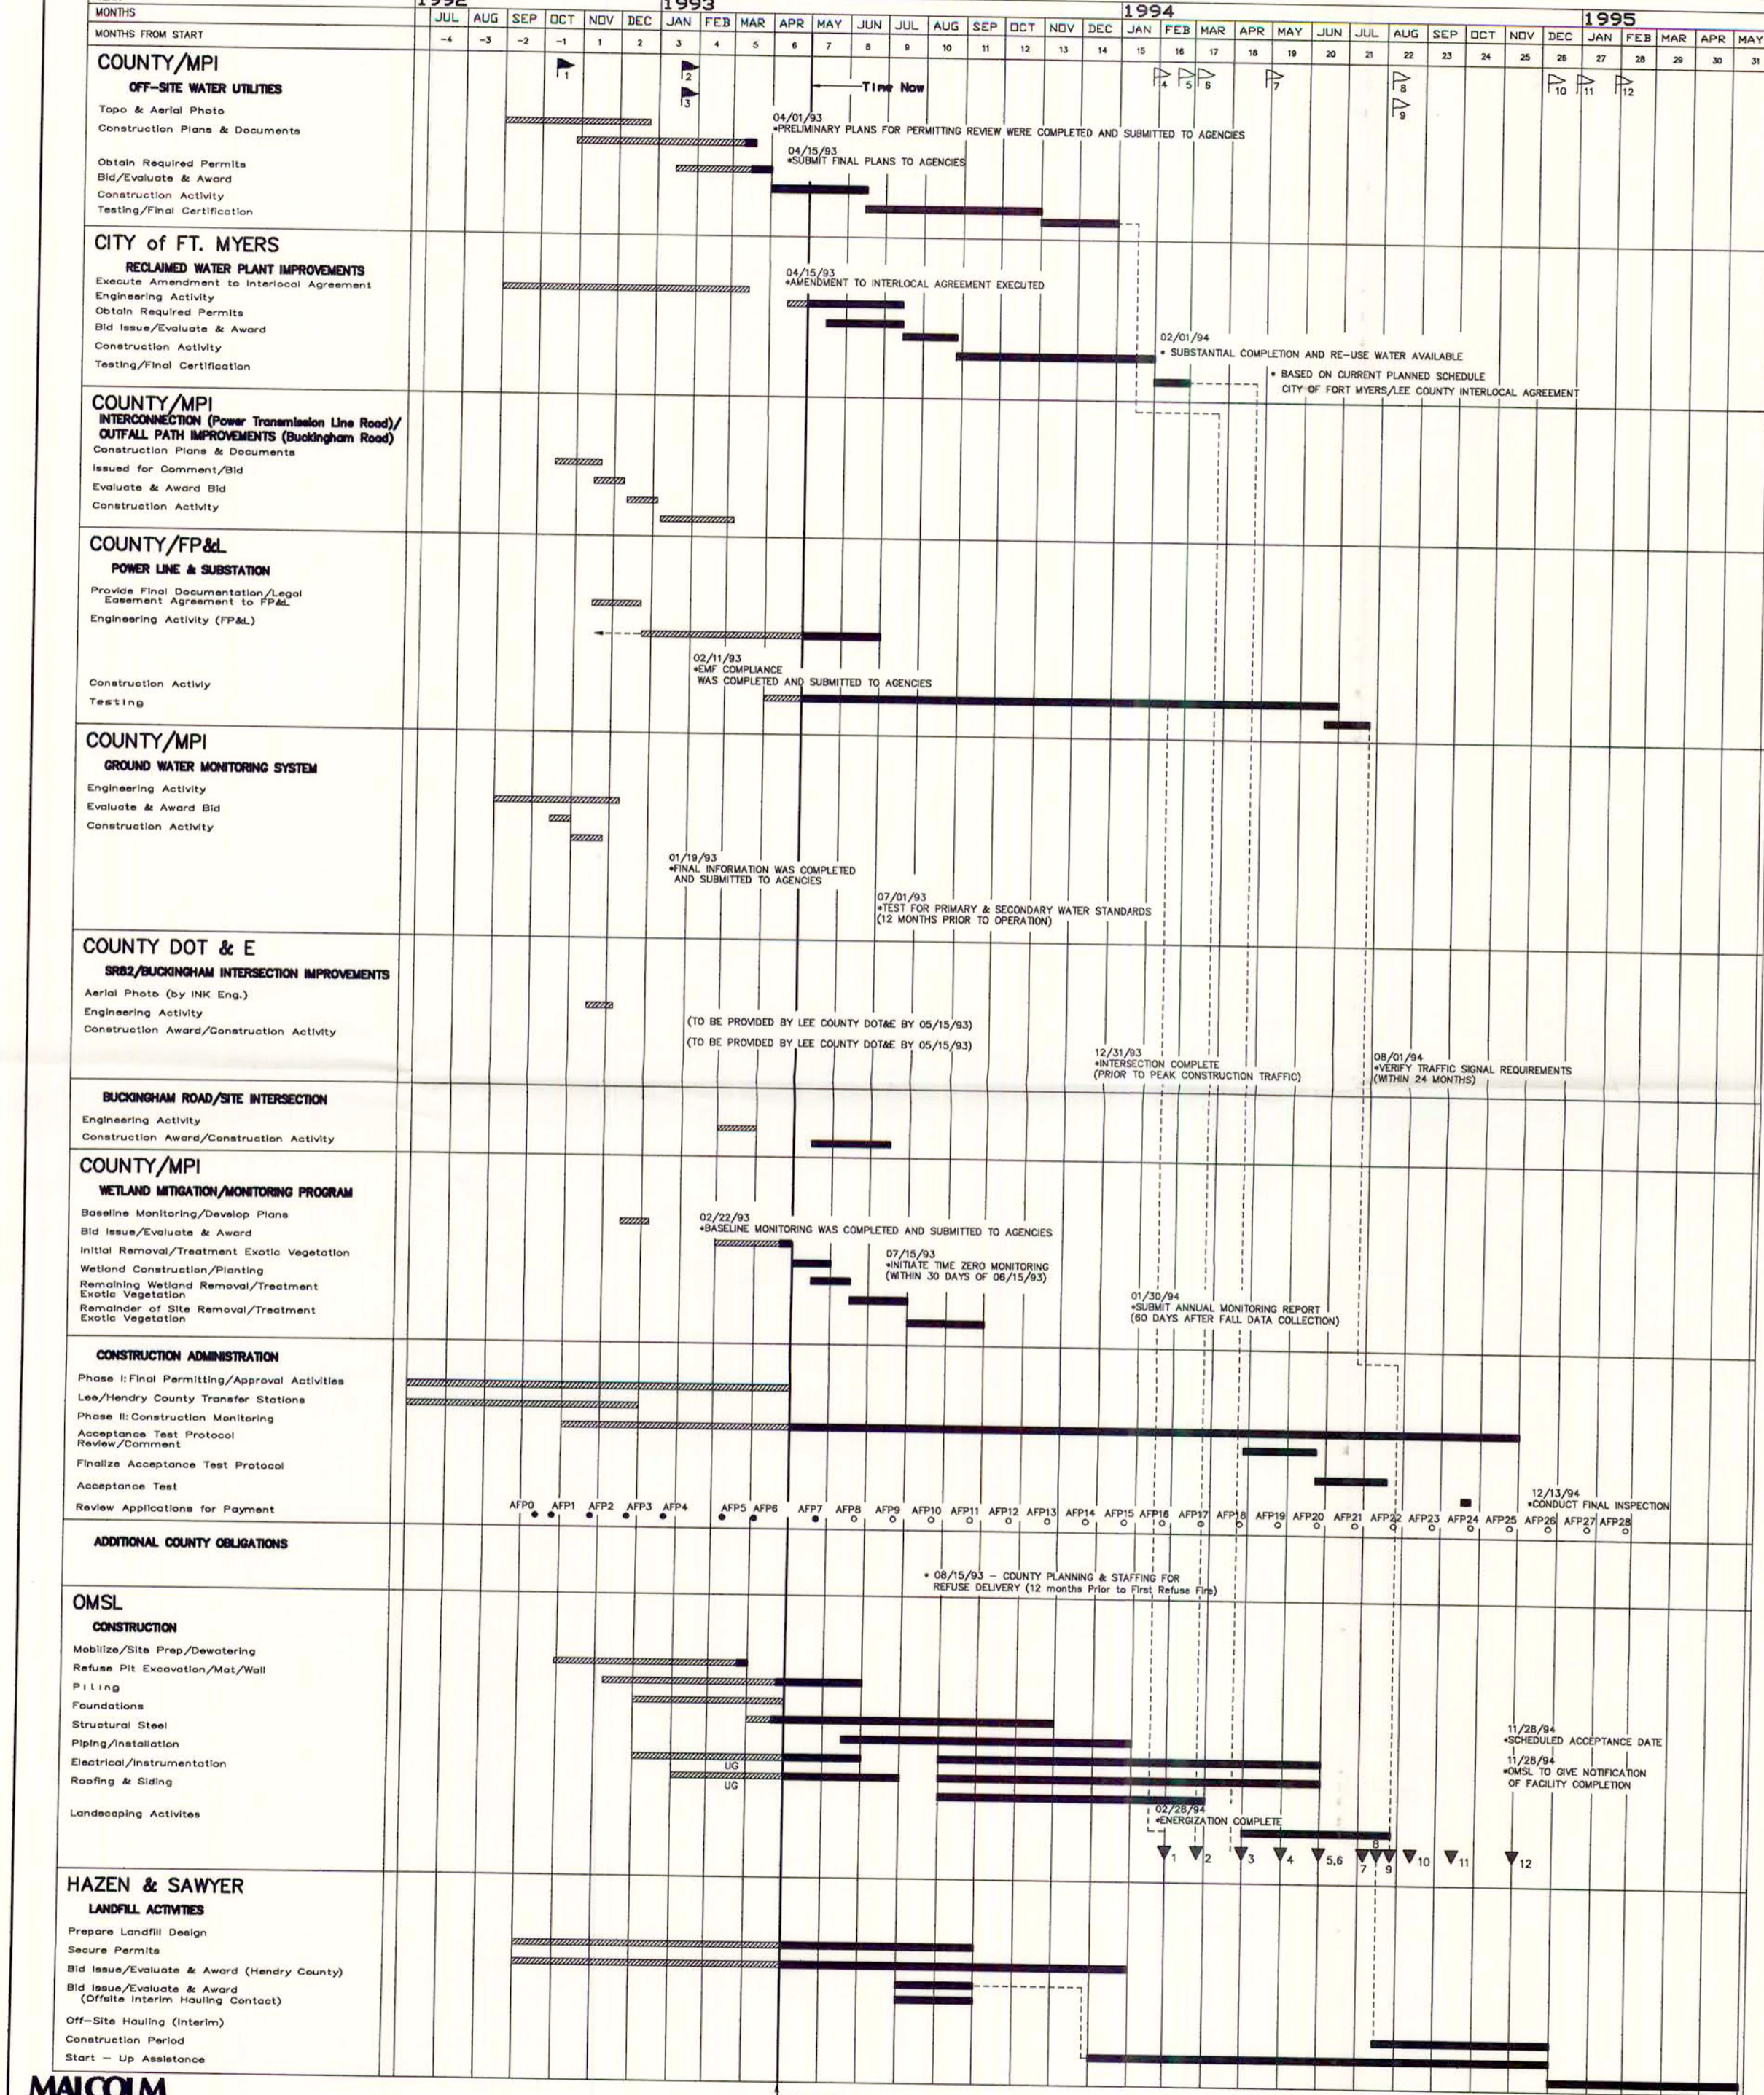

- LEGEND**
- ▽ MILESTONE
 - ▬ MILESTONE COMPLETED
 - ▬ SCHEDULED ACTIVITY
 - ▨ ACTIVITY PROGRESS
 - EARLY START
 - APP SCHEDULED
 - APP COMPLETED

- LEE COUNTY MILESTONES**
- NOTICE TO PROCEED - 10/28/92
 - FLL THROUGH JURISDICTIONAL WETLANDS COMPLETE (TRANSMISSION LINE ROAD) - 07/21/93
 - FINAL GROUNDWATER MONITORING INFORMATION TO FP&L - 01/22/93
 - OFF-SITE UTILITIES IN SERVICE FOR FACILITY - 01/31/94
 - START-UP POWER FROM FP&L AVAILABLE - 02/23/94
 - SR82/BUCKINGHAM ROAD INTERSECTION IMPROVEMENTS COMPLETED - 02/07/94
 - ACCEPTANCE TEST PLAN (OMSL) TO SUBMIT TO COUNTY - 04/28/94
 - FP&L INTERCONNECTION COMPLETED - 08/01/94
 - INTERIM ASH DISPOSAL/HAULING CONTRACT IN PLACE - 08/01/94
 - COLD IRON OUTAGE INSPECTION - 12/05/94
 - RECEIVE OMSL FINAL ACCEPTANCE TEST RESULTS - 12/28/94
 - FINAL FACILITY APPROVAL - 01/23/95 (WITHIN 30 DAYS OF RECEIVING CONTRACTOR'S CERTIFICATION)

- ODDEN MARTIN SYSTEM OF LEE SYSTEM START-UP MILESTONES**
- ENERGIZATION 18 MOS
 - DEMINERALIZER SYSTEM STARTUP 18 3/4 MOS
 - START-UP PRE-BLOWER SYSTEM FLUSH 18 MOS
 - BALANCE/RUN-IN BOILER FANS AND DRAFT CONTROLS 19 MOS
 - FIRST FIRE/BOILOUT 20 MOS
 - MAIN TURBINE LO FLUSH COMPLETE 20 MOS
 - START COMMON STEAM BLOWS 21 1/4 MOS
 - FIRST REFUSE FIRE 21 1/2 MOS
 - INITIAL GENERATOR ENERGIZATION 21 3/4 MOS
 - START PLANT TESTING/FULL LOAD RUN 22 1/4 MOS
 - START PLANT ACCEPTANCE TESTING 23 1/2 MOS
 - READY FOR COMMERCIAL OPERATION 25 MOS

DRAW DOWN SCHEDULE

APP#	CUMULATIVE PERCENTAGE OF FACILITY PRICE
APP0	3.30 %
APP1	4.65 %
APP2	6.35 %
APP3	9.25 %
APP4	14.00 %
APP5	18.40 %
APP6	22.90 %
APP7	28.50 %
APP8	33.75 %
APP9	38.75 %
APP10	46.00 %
APP11	51.95 %
APP12	57.70 %
APP13	64.20 %
APP14	68.70 %
APP15	73.90 %
APP16	77.90 %
APP17	83.00 %
APP18	85.25 %
APP19	87.25 %
APP20	88.15 %
APP21	88.95 %
APP22	89.75 %
APP23	90.00 %
APP24	93.00 %
APP25	96.00 %
APP26	96.00 %
APP27	100.00 %

REVISIONS

REV #	DATE	DESCRIPTION
REV 0	12/18/92	ISSUED FOR COMMENT
REV 1	01/29/93	INCORPORATES PROJECT TEAM COMMENTS
REV 2	02/28/93	STATUS THROUGH 2/28/93
REV 3	03/21/93	STATUS THROUGH 3/21/93
REV 4	04/30/93	STATUS THROUGH 4/30/93 - REFLECTS CITY OF FORT MYERS UPDATED RECLAIMED WATER PLANT IMPROVEMENT SCHEDULE

MALCOLM PIRNIE

LEE COUNTY DIVISION OF SOLID WASTE MASTER PROJECT SCHEDULE
